










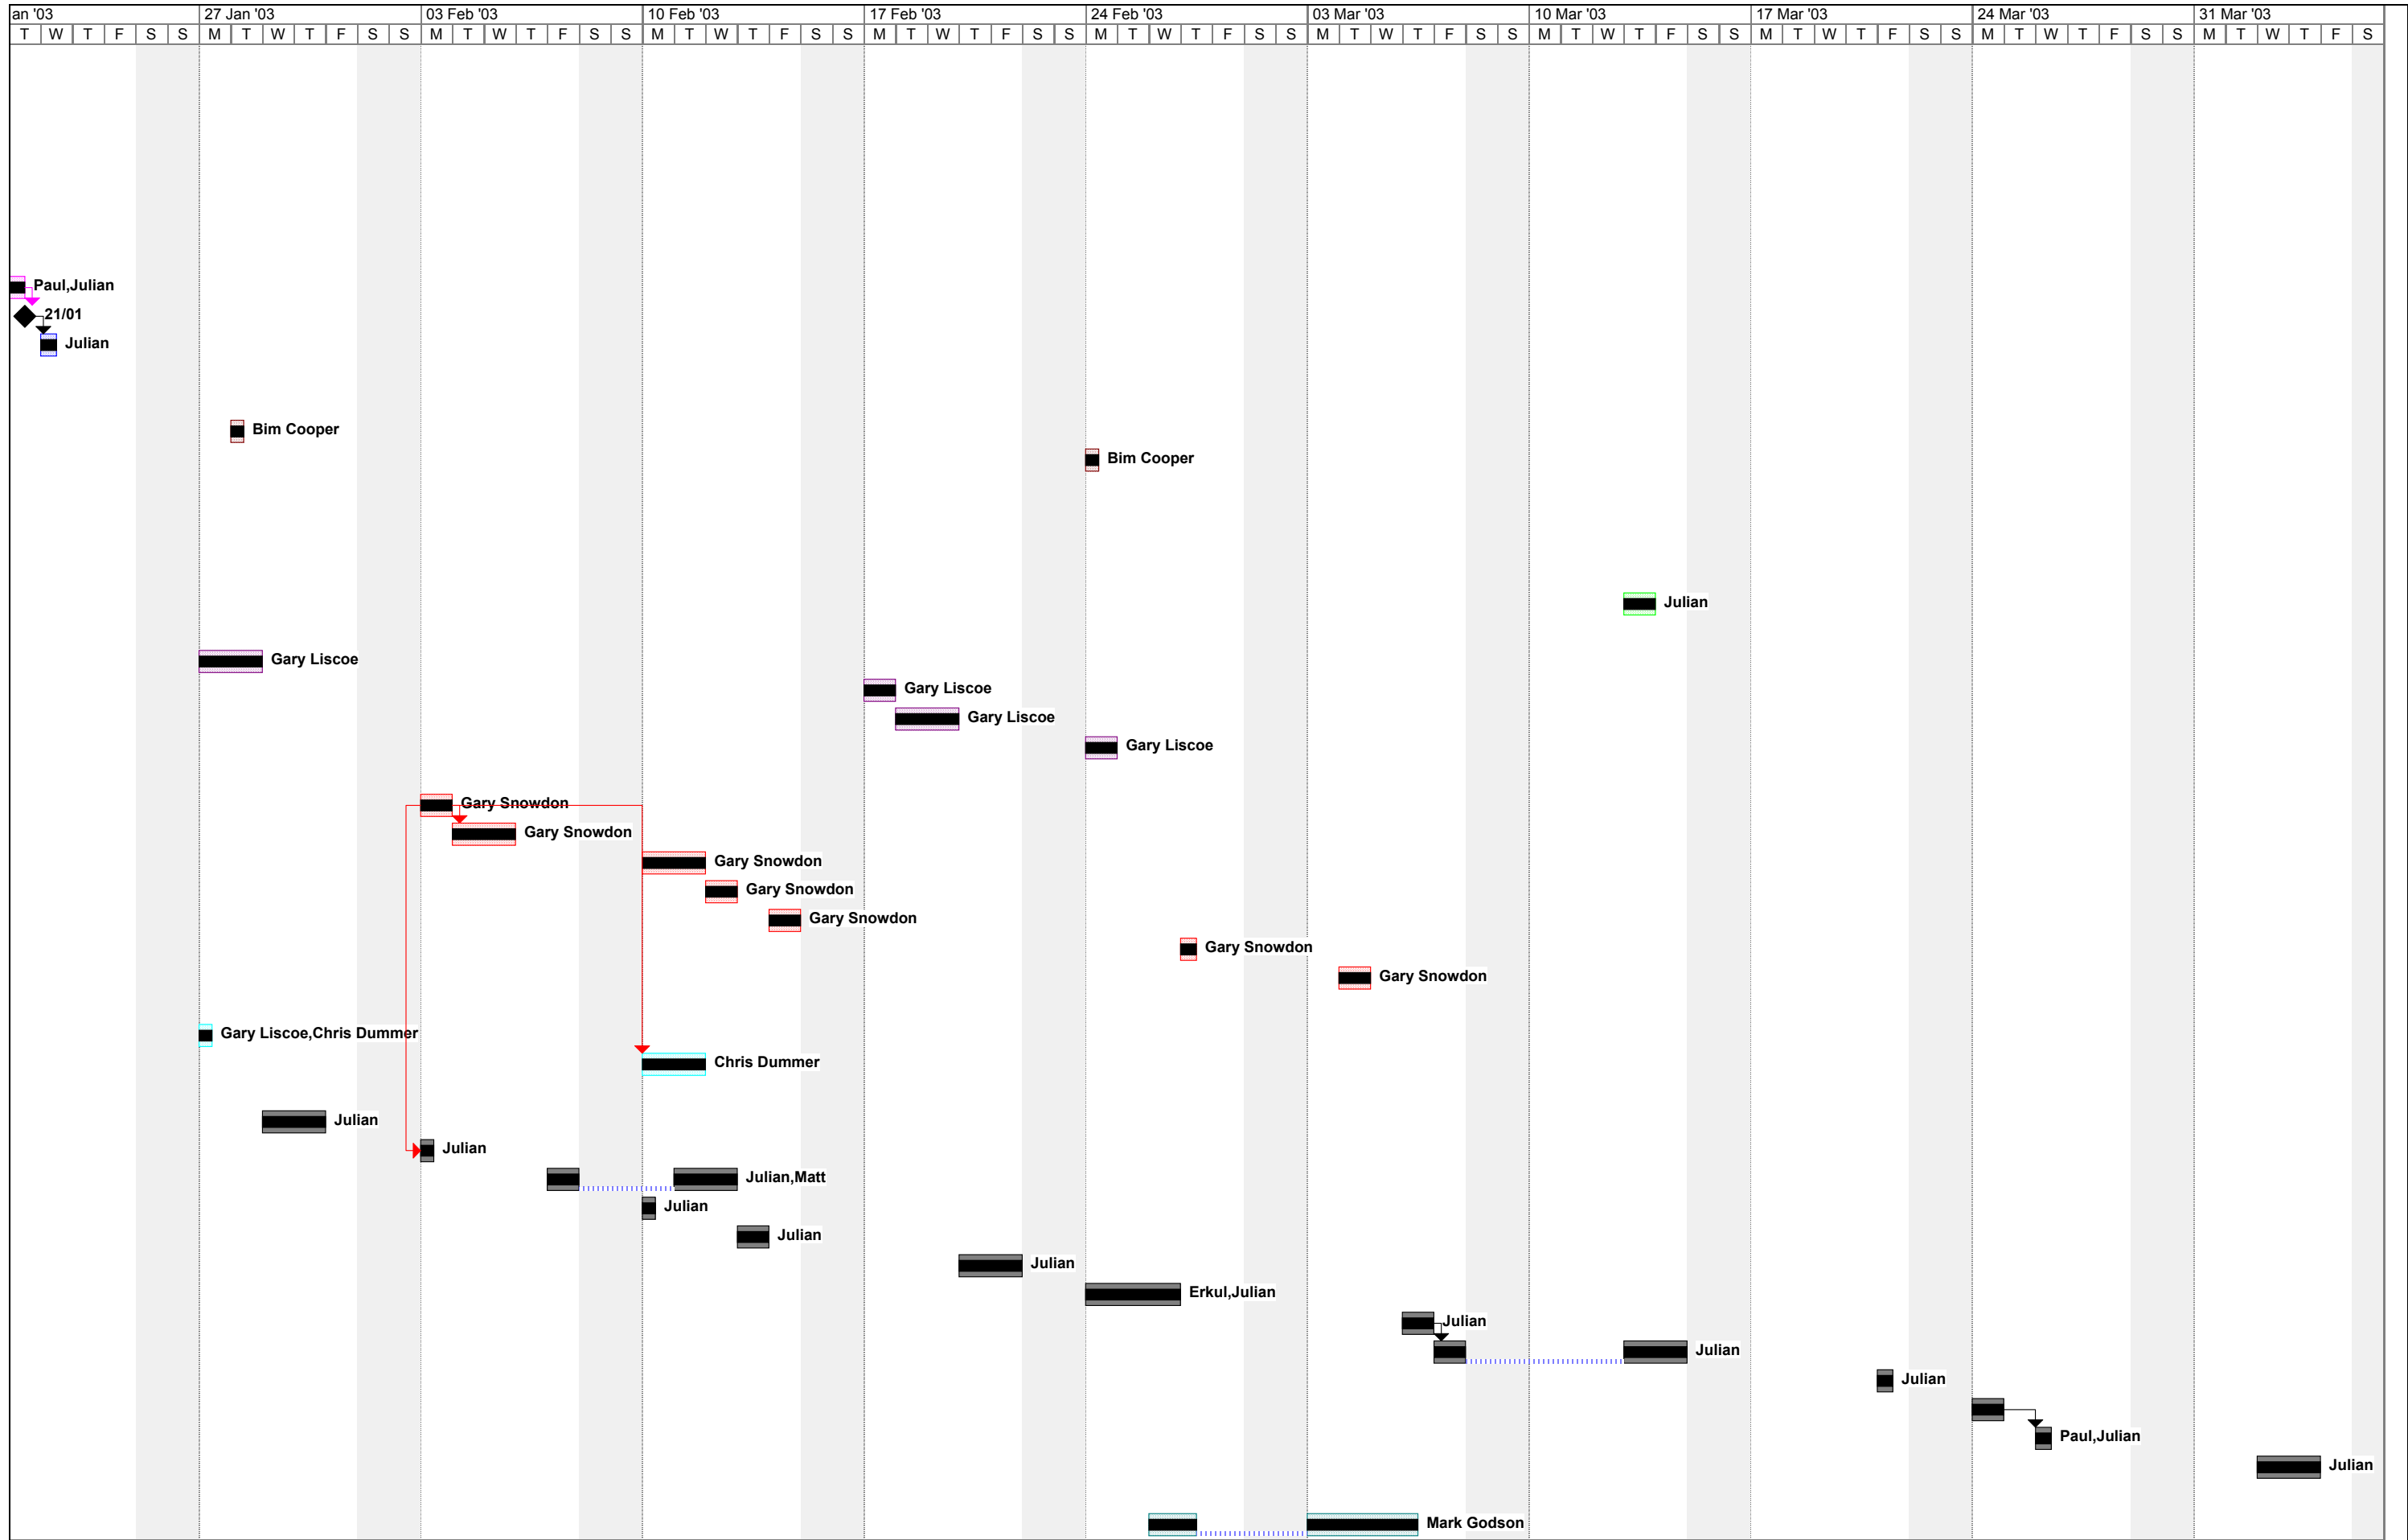


ID	Task Name	Duration	25 Nov '02			02 Dec '02			09 Dec '02			16 Dec '02			23 Dec '02			30 Dec '02			06 Jan '03			13 Jan '03			20																							
			S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F
1	✓ Proposal	7 days																																																
2	✓ Presentation	0.25 days																																																
3	✓ 3D CAD Design	1 day																																																
4	✓ Finalised Quotation	0.25 days																																																
5	✓ Quotation Accepted	0 days																																																
6																																																		
7	✓ Project Schedule	2 days																																																
8	✓ Autocad Room Design	1 day																																																
9	✓ Final meeting before work commences	0.5 days																																																
10	✓ Second Payment	0 days																																																
11	✓ Cable Schedule	0.5 days																																																
12																																																		
13	✓ Interior Designer	0.25 days																																																
14	✓ Meeting with Bim / Interior Layout	0.25 days																																																
15	✓ Interior Designer Meeting With Decorator	0.25 days																																																
16																																																		
17	✓ Blinds / Interior Designer Site Meeting	0.25 days																																																
18	✓ Blind Quotation	0.25 days																																																
19	✓ Site Visit Re Blinds and RF System	0.25 days																																																
20	✓ Blind Installation	1 day																																																
21																																																		
22	✓ Lower ceiling	2 days																																																
23	✓ Light Fitting Cut Outs	1 day																																																
24	✓ Both Ceiling and Plastering	2 days																																																
25	✓ Projector Screen Pelmit	1 day																																																
26																																																		
27	✓ Mains supply to air conditioning unit	1 day																																																
28	✓ Room Mains Distribution	2 days																																																
29	✓ Lighting wiring	2 days																																																
30	✓ Floor Box (Network Telephone Audio Video)	1 day																																																
31	✓ Cable Distribution	1 day?																																																
32	✓ RF Mains Supply	0.5 days																																																
33	✓ Fitting Lights & Face Plates	1 day																																																
34																																																		
35	✓ Site Meeting Chris D and Gary L	0.25 days																																																
36	✓ Air conditioning installation	2 days																																																
37																																																		
38	✓ Order Equipment	2 days																																																
39	✓ Site meeting with Gary S	0.25 days																																																
40	✓ Setup and Programming	3 days																																																
41	✓ Site Visit	0.25 days																																																
42	✓ Test	1 day																																																
43	✓ Lighting System	2 days																																																
44	✓ RF distribution	3 days																																																
45	✓ Speaker Installation	1 day																																																
46	✓ Headend install	3 days																																																
47	✓ Client Meeting	0.5 days																																																
48	✓ System Changes	1 day																																																
49	✓ Client/System Run Through	0.5 days																																																
50	✓ Finally programming control system and cal	2 days?																																																
51																																																		
52	✓ Decorating	5 days																																																

Project: js-byng-03.01.21  
Date: Tue 07/10/03

Task  Milestone  Rolled Up Task  Rolled Up Progress  External Tasks  Group By Summary 

Progress  Summary  Rolled Up Milestone  Split  Project Summary 



Project: js-byng-03.01.21  
Date: Tue 07/10/03

Task		Milestone		Rolled Up Task		Rolled Up Progress		External Tasks		Group By Summary	
Progress		Summary		Rolled Up Milestone		Split		Project Summary			
